



● Status & Critical Path

What is done, and what is left


The marketing site is live and public today. The platform passes its own contract and invariant suites on every run. What stands between here and taking real orders is three items — most of it account setup measured in hours — and the long-lead blocker everyone has been bracing for turns out not to apply.

DATE	WEBSITE	V1 FEATURES COMPLETE	STAGE ONE OPENS	START TODAY
21 Sep 2026	Live & public	158 / 191	Mon 5 Oct	D-U-N-S number

DELIVERED

The website is live, and you can open it right now

Seven pages, a desktop and a phone layout each, verified against the **deployed** build this morning rather than against a local copy.

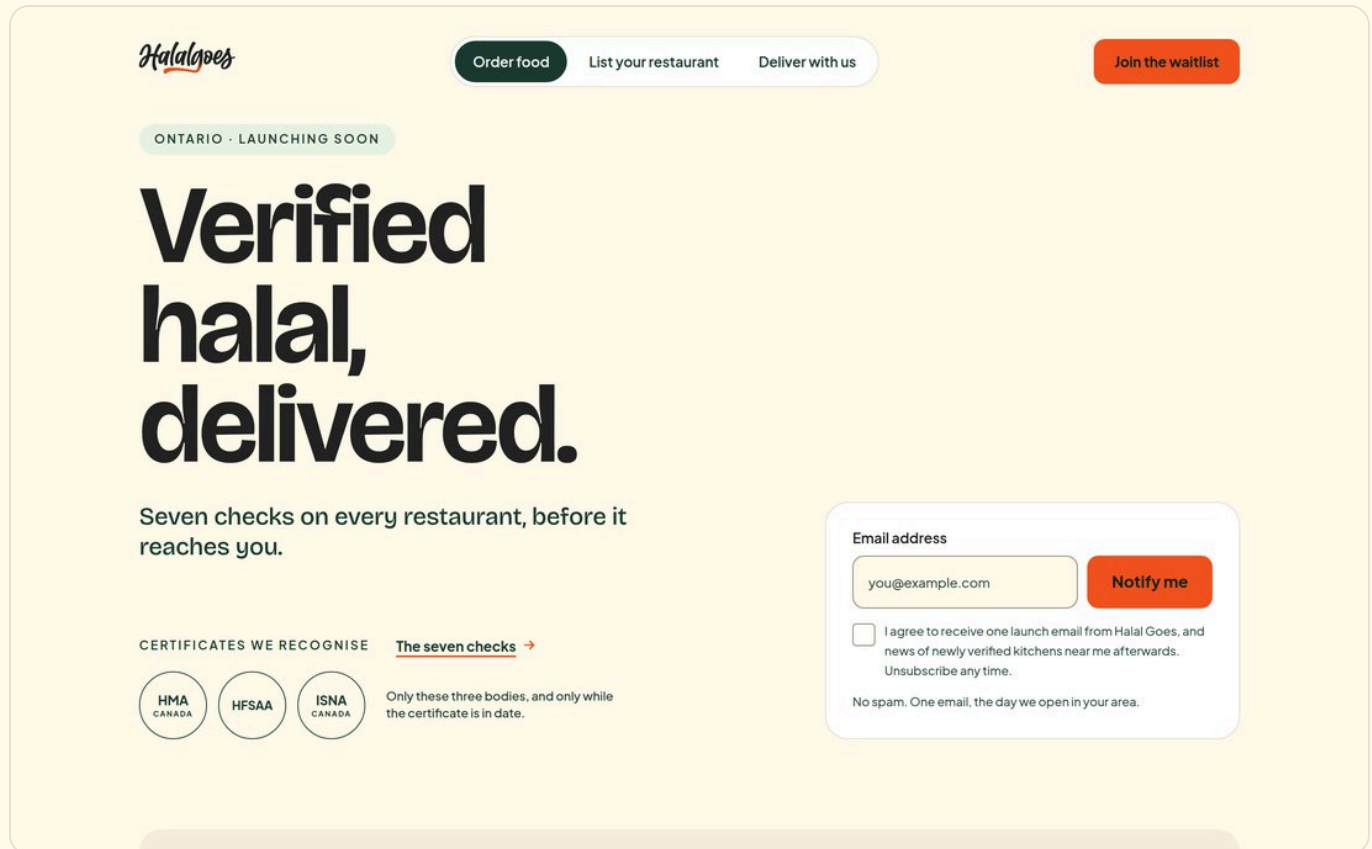

Checked at 1440 px and 390 px across `/`, `/restaurants`, `/riders`, `/verification`, `/blog`, `/privacy` and `/terms`. All fourteen combinations returned 200 with **zero** horizontal scroll, **zero** broken images and **zero** console errors.

One decision we need from you: the domain

- `halalgoes.com` points at the first site, on its own hosting project.
- A domain belongs to one project at a time — release it there, point it here.
- A few minutes in the dashboard, then DNS. A switch, not a rebuild.
- The first site held the name and collected early interest. This is its next version: the published standard, a page per audience, privacy and terms, and a consent-wired waitlist.

THE PLATFORM UNDERNEATH

The engine is built, and it re-proves itself on every run

152/152

CONTRACT OPERATIONS
CONFORM

18/18

MONEY & SAFETY
INVARIANTS

158/191

FEATURES COMPLETE

330

FIXTURES, EVERY STATE

The other 33 are 29 deliberately deferred to a later version and 4 partial. None of this is self-assessment: the contract suite runs every published API operation against its declared shape, and the invariant suite runs against a real database — every order's money decomposing to zero residual, no order state able to wait forever, a missing `halal` field rendering no badge rather than an optimistic one.

The blocker we have been planning around does not apply

Our own decision log has carried this line for months: *“SMS / A2P registration — nobody can sign in without it. Approval takes days to weeks. The longest lead time in the project.”* We checked it against the carrier documentation this morning rather than taking it on trust.

It was written against the wrong country, and the wrong channel

- **A2P 10DLC does not govern WhatsApp at all.** It covers SMS sent from ten-digit long codes to **United States** recipients. Other channels are out of its scope entirely.
- **The product already defaults to WhatsApp.** Not a change we are proposing — the sign-in code was written this way and ships that way today, with SMS as the alternative.
- **This is an Ontario launch.** For Canada-to-Canada messaging the registration is not mandatory. It remains worth completing so the SMS fallback delivers reliably, but it is an improvement, not a gate.
- **The business verification it does depend on is already done.** Confirmed today.

Net effect: the item we had priced at “days to weeks, and nothing ships without it” is off the critical path.

WHAT IS ACTUALLY LEFT

What is left, and who holds each piece

GATE	OWNER	TIME	STATE
Cloud account with billing So the platform has somewhere to run. We provision, configure and secure it from there.	You then us	Hours from you 1-2 days from us	Needed
Live payment keys Held up by the account-access problem on Stripe’s side that we raised with you earlier. The payment code is written and already runs against their sandbox, so live keys are a configuration change rather than development work.	Stripe we are chasing	Open with them	Raised
Messaging account details Account identifiers for the sign-in codes. The sender itself is already verified.	You	Hours	Confirm
Domain release Point halalgoes.com here. Released from its current project first, since a domain can only belong to one.	You	Minutes + DNS propagation	Your call
Verification pass across the apps Runs alongside everything above and does not wait on any of it.	Us	In progress	Underway
App store developer accounts Organisation, not individual. Gated on a D-U-N-S number, which is the one genuinely long item left. Stage one does not need any of it.	You	5-30 days for the D-U-N-S	Start today
SMS carrier registration	—	—	Not a gate

One line here is a genuine queue we cannot shorten — the D-U-N-S, which is exactly why it wants starting today rather than on the day the stores are needed. Every other line is an account you open or work already running.

THE PLAN

Open in two stages, not one

Restaurants and administrators sign in with email and password. Customers and riders sign in with a code to their phone. Those are two different systems, and only the second depends on messaging — which is what lets the first stage open without waiting on anything but hosting.

STAGE ONE — MONDAY 5 OCTOBER

Restaurants onboard, we verify

- Restaurants apply and upload real certificates.
- Our reviewers run the seven checks. Listings go live.
- No customer orders yet.

The central claim, exercised on real documents before anyone relies on it for dinner.

Depends on: the cloud account, and nothing else. With it in hand by **Wednesday 30 September**, this date holds.

STAGE TWO — WHEN STAGE ONE IS STABLE

Customers order, riders deliver

- Ordering, payment, dispatch, live tracking, payouts.
- Opens once stage one's restaurants are on and keys are live.

Every listing a customer sees has already been through the instrument.

Depends on: the Stripe access clearing, messaging details, and stage one holding.

Why two stages rather than one date

- One launch puts an untested surface in front of paying customers on day one.
- Staged, the first users are restaurant owners and our reviewers — they can flag a fault without it costing anyone a meal.
- A wrong halal badge is not a defect to patch next sprint. It is a harm we cannot take back.
- And it is a date we can hold.

THIS WEEK

Five defects found and fixed, by using the apps rather than testing them

Capturing the screenshots on the previous page meant driving all four applications end to end. That found things every automated check had passed over.

WHAT	WHY IT MATTERED	STATE
Admin console could not sign in	A diagnostic message containing a character the underlying protocol forbids crashed the response it was attached to, on every request. The console that runs the seven checks could not be opened against test data at all — very likely why a large share of features sat marked “not yet verified”: nobody could reach them.	Fixed
Restaurant payouts page went blank	A missing guard took down not just the page but the whole application shell, navigation included.	Fixed
Customer app's first screen unreadable	The title on the home screen measured 1.28:1 against its background. Legibility requires 4.5:1. Dark text had been placed on a dark bar — the first thing every customer sees.	Fixed
Rider app showed internal debug text	A raw internal value was rendering to riders in the live build.	Fixed
Low-contrast grey across both phone apps	One shared colour fails the legibility standard in several places. It is a foundational value used everywhere, so it is being changed deliberately rather than patched per screen.	Scheduled

Two lists, and one of them starts today

The first is ours and needs nothing from anyone. The second is yours — and one item on it now has a longer lead time than anything else left in this project.

Ours, starting immediately

WORK	DETAIL
Manual verification pass, all four apps	This is what turns “built” into “tested”. It was partly blocked until this week — the console fault on the previous page meant the administrative surface could not be driven end to end at all. That is fixed, so the pass can now cover everything.
Store listing preparation	Screenshots, descriptions, privacy declarations, content ratings and signed builds. None of it needs the developer accounts to exist, so all of it will be ready and waiting — submission becomes same-day once the accounts open.
Production provisioning	Written and rehearsed, ready to execute the hour the cloud account exists.

Yours, and the order matters

	ACTION	WHY NOW
1	Start a D-U-N-S number today Free, from Dun & Bradstreet	This is the longest lead time left in the project. Up to five business days if your entity is already on file — up to thirty if it is not . Both app stores need it to register you as an organisation. Nothing else on this list takes as long, and nothing else can be started as cheaply. It costs nothing to begin it this afternoon.
2	Approve the site	Until the pages are signed off we cannot scope the manual pass against a settled surface, and until that is scoped we cannot give you a production date worth holding us to. This is the item that unlocks the estimate.
3	Register the stores as an organisation	Not as an individual. A personal Google Play account opened since late 2023 must run a closed test with twelve testers for fourteen continuous days before it may publish. Organisation accounts publish straight to production. The account type is worth two weeks.
4	Cloud account with billing	The only thing between today and stage one on 5 October.
5	The Stripe account access Already raised with you	This is the issue we flagged rather than a new one: the sign-in fails, so the live keys cannot be retrieved. It sits with Stripe and we are pursuing it. If it has not moved by the time stage one opens, the fallback is a fresh platform account on the same entity — a day’s work, and one we would rather not spend, so the decision point is worth naming now rather than discovering later. Nothing in stage one touches payments.
6	Messaging account credentials	The sender itself is already verified. We need the account identifiers and the verification service, which is a copy-and-paste from your dashboard.
7	The domain, when you are ready	The site is live and shareable today regardless.

Stage one waits for none of the store work

Restaurant onboarding and halal verification run in the browser. No app store, no developer account, no review queue, no D-U-N-S. That is the second reason to open in two stages: the half of the product that carries the claim ships on a timeline nobody outside this room controls, while the store clock runs in parallel for stage two.

Why there is no production date in this document

- 1. You approve the site.
- 2. We scope the manual pass against a surface that has stopped moving.
- 3. We give you a date, with the store lead time on top — one we can hold.

A number produced before those three is a guess, and you have had enough of those.
