



● Status & Critical Path

What is done, and what is left


The marketing site is live and public today. The platform passes its own contract and invariant suites on every run. What stands between here and taking real orders is three items — most of it account setup measured in hours — and the long-lead blocker everyone has been bracing for turns out not to apply.

DATE	WEBSITE	V1 FEATURES COMPLETE	REMAINING GATES	LONGEST LEAD TIME
21 Sep 2026	Live & public	158 / 191	3	Days, not weeks

DELIVERED

The website is live, and you can open it right now

Seven pages, a desktop and a phone layout each, verified against the **deployed** build this morning rather than against a local copy.

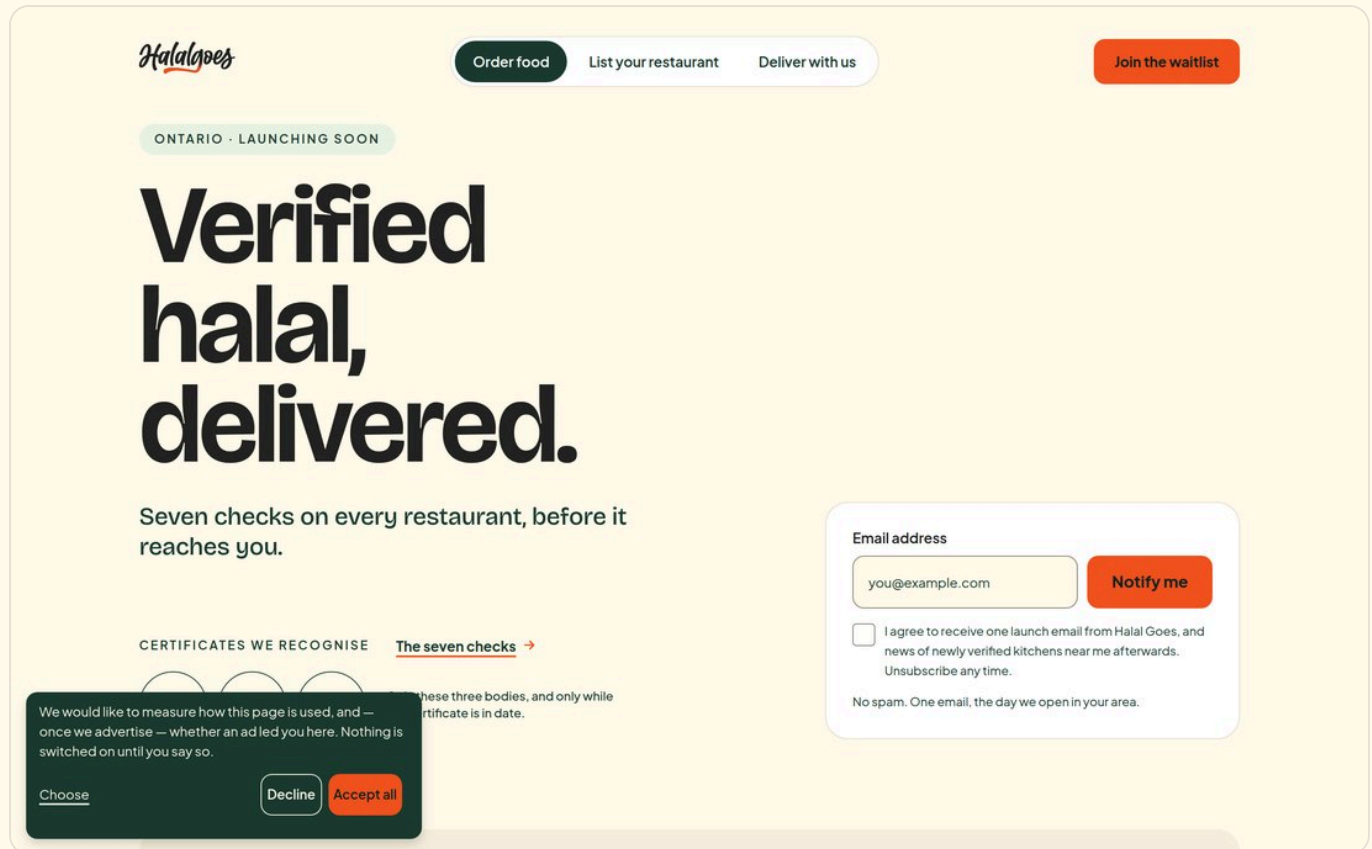

Checked at 1440 px and 390 px across `/`, `/restaurants`, `/riders`, `/verification`, `/blog`, `/privacy` and `/terms`. All fourteen combinations returned 200 with **zero** horizontal scroll, **zero** broken images and **zero** console errors.

One decision we need from you: the domain

halalgoes.com still points at the **previous** site, which lives on a separate hosting project. A domain can belong to only one project, so moving it means releasing it from the old one. That is your call to make, not ours.

Worth knowing what is on it today: the hero headline renders in a tone close to unreadable against its own background, three images are broken including the logo, and it carries the claims “100% halal-certified” and “Verified for authenticity”. Neither is backed by a source we could put in front of a regulator. The new site states only what the seven checks actually establish.

THE PLATFORM UNDERNEATH

The engine is built, and it re-proves itself on every run

152/152

CONTRACT OPERATIONS
CONFORM

18/18

MONEY & SAFETY
INVARIANTS

158/191

FEATURES COMPLETE

330

FIXTURES, EVERY STATE

The other 33 are 29 deliberately deferred to a later version and 4 partial. None of this is self-assessment: the contract suite runs every published API operation against its declared shape, and the invariant suite runs against a real database — every order’s money decomposing to zero residual, no order state able to wait forever, a missing halal field rendering no badge rather than an optimistic one.

The one screen that carries the whole promise

Everything on the next two pages is a screenshot taken this morning from the applications themselves, driven end to end — signing in, loading data, moving between screens. Nothing here is a mock-up.

Halal Goes — Admin

Restaurants

Riders

Orders

Refunds & disputes

System

Staff

< Back

Halal verification

Seven mandatory checks (A-15). Approval is only possible once all seven pass; H5 and H7 are computed by the server and cannot be overridden.

Certificate under review

Certified name
Karachi Kitchen Inc.

Issuing body
Halal Munchies Scarborough

Certificate no.
HMA-ON-46160

Status
APPROVED

Halal certification checklist

Every value you record here, and every decision, is written to the audit log with your identity and the time.

Certificate number
HMA-ON-46160

Issuing body
Halal Munchies Scarborough

Certified legal name
Karachi Kitchen Inc.

Certified address
1245 Danforth Avenue, Toronto, ON M4J 1M4

Issued on
9 March 2026

Expires on
9 March 2027

Scope
Whole establishment

H1 Legible complete

The scan is legible, all pages are present, and there is no visible alteration.

System suggested: **Pass**. Changing it requires a note.

✓ Pass

Fail

Not assessed

Note (optional)

0/20 characters

Record H1

H2 Issuer accepted

The issuing body is **ACCEPTED** in the registry at this moment.

System suggested: **Pass**. Changing it requires a note.

✓ Pass

Fail

Not assessed

Note (optional)


The verification instrument. Seven mandatory checks against the certificate, each recorded against a named reviewer and a timestamp. Two of them — H5, that the dates are valid, and H7, that this certificate is not already in use by a different restaurant — are computed by the server and **cannot be overridden**. The screen says so in plain words: *“No one can override it, including a Super Admin.”* Approval is impossible until all seven pass.

This is the difference between a platform that promises halal and one that can show its working. The rule is not in a policy document that someone could decide to bend on a busy evening; it is in the software, and the software will not bend.

The other three surfaces




Admin — onboarding queue. Applications oldest first, with the review deadline tracked per row so nothing sits unattended.



Restaurant — live orders. Alongside menu, trading hours, payouts, staff and settings.



Customer. Every listing carries the certified badge — because a kitchen that has not passed the seven checks is never listed at all. There is no “probably halal” state for a customer to misread.

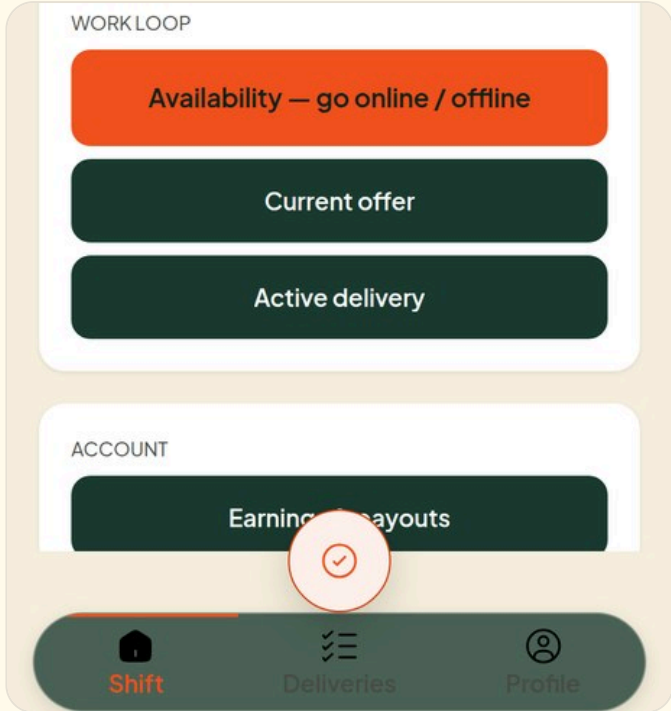

Rider. Going on and off shift, the current offer and the active delivery, with earnings, history and documents behind the account section.

The blocker we have been planning around does not apply

Our own decision log has carried this line for months: *“SMS / A2P registration — nobody can sign in without it. Approval takes days to weeks. The longest lead time in the project.”* We checked it against the carrier documentation this morning rather than taking it on trust.

It was written against the wrong country, and the wrong channel

- **A2P 10DLC does not govern WhatsApp at all.** It covers SMS sent from ten-digit long codes to **United States** recipients. Other channels are out of its scope entirely.
 - **The product already defaults to WhatsApp.** Not a change we are proposing — the sign-in code was written this way and ships that way today, with SMS as the alternative.
 - **This is an Ontario launch.** For Canada-to-Canada messaging the registration is not mandatory. It remains worth completing so the SMS fallback delivers reliably, but it is an improvement, not a gate.
 - **The business verification it does depend on is already done.** Confirmed today.
- Net effect: the item we had priced at “days to weeks, and nothing ships without it” is off the critical path.**

WHAT IS ACTUALLY LEFT

Three gates, and most of the clock is account setup

GATE	OWNER	TIME	STATE
Cloud account with billing So the platform has somewhere to run. We provision, configure and secure it from there.	You then us	Hours from you 1-2 days from us	Needed
Live payment keys Business entity, bank account and payout onboarding. The payment code is written and tested against the sandbox.	You	Hours to days	Needed
Messaging account details Account identifiers for the sign-in codes. The sender itself is already verified.	You	Hours	Confirm
Domain release Point halalgoes.com at the new site. Needs releasing from the old hosting project first.	You	Minutes + DNS propagation	Your call
Verification pass across the apps Runs alongside everything above and does not wait on any of it. See overleaf.	Us	In progress	Underway
SMS carrier registration	—	—	Not a gate

Nothing on this list is a queue we sit in. Every line is either an account you open or work already running.

THE PLAN

Open in two stages, not one

Restaurants and administrators sign in with email and password. Customers and riders sign in with a code to their phone. Those are two different systems, and only the second depends on messaging — which is what lets the first stage open without waiting on anything but hosting.

STAGE ONE — MONDAY 5 OCTOBER

Restaurants onboard, we verify

Real restaurants apply, upload real certificates, and our reviewers run the seven checks against them. Listings are created and approved.

No customer orders yet. This is the product's central claim being exercised on real documents, before anyone is relying on it for dinner — and it needs nothing from the messaging stack.

Depends on: the cloud account, and nothing else. With it in hand by **Wednesday 30 September**, this date holds.

STAGE TWO — WHEN STAGE ONE IS STABLE

Customers order, riders deliver

Full service: ordering, payment, dispatch, live tracking, payouts.

Opens once the verified restaurants from stage one are on the platform and the payment keys are live. By then every listing a customer sees has already been through the instrument.

Depends on: payment keys, messaging details, and stage one holding.

Why two stages rather than one date

A single launch puts the untested surface in front of paying customers on day one. Staging it means the first people to exercise the system are restaurant owners and our own reviewers, who can tell us something is wrong without it costing anyone a meal. On a platform whose entire promise is halal verification, a wrong badge is not a defect to patch next sprint — it is a harm we cannot take back. The staged opening is also a date we can actually hold.

THIS WEEK

Five defects found and fixed, by using the apps rather than testing them

Capturing the screenshots on the previous page meant driving all four applications end to end. That found things every automated check had passed over.

WHAT	WHY IT MATTERED	STATE
Admin console could not sign in	A diagnostic message containing a character the underlying protocol forbids crashed the response it was attached to, on every request. The console that runs the seven checks could not be opened against test data at all — very likely why a large share of features sat marked “not yet verified”: nobody could reach them.	Fixed
Restaurant payouts page went blank	A missing guard took down not just the page but the whole application shell, navigation included.	Fixed
Customer app's first screen unreadable	The title on the home screen measured 1.28:1 against its background. Legibility requires 4.5:1. Dark text had been placed on a dark bar — the first thing every customer sees.	Fixed
Rider app showed internal debug text	A raw internal value was rendering to riders in the live build.	Fixed
Low-contrast grey across both phone apps	One shared colour fails the legibility standard in several places. It is a foundational value used everywhere, so it is being changed deliberately rather than patched per screen.	Scheduled

What we need from you, in order

- **The cloud account.** The only thing standing between today and stage one.
- **Payment account details.** Can run in parallel; needed for stage two.
- **A decision on the domain.** The new site is live and public today either way.

The cloud account is the one that moves the date. Everything else can run in parallel; that one cannot start until it exists.
